


# A285 Route Improvements

ID	Task Name	Duration	Start	Finish	Predecessors	Half 1, 2017					Half 2, 2017					Half 1, 2018					Half 2, 2018					Half 1, 2019									
						N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A
1	<b>A285 Improvements (Phase 1)</b>	<b>452 days?</b>	<b>Thu 01/12/16</b>	<b>Fri 24/08/18</b>		A285 Improvements (Phase 1)																													
62																																			
63	<b>A285 Improvements (Phase 2)</b>	<b>378 days?</b>	<b>Wed 01/11/17</b>	<b>Fri 12/04/19</b>		A285 Improvements (Phase 2)																													
64	<b>Detailed Design</b>	<b>77 days</b>	<b>Wed 01/11/17</b>	<b>Fri 16/02/18</b>		Detailed Design																													
65	Carry Out Detailed Design	13 wks	Wed 01/11/17	Tue 30/01/18		Carry Out Detailed Design																													
66	Stage 1/2 Safety Audit	5 days	Mon 05/02/18	Fri 09/02/18	65FF	Stage 1/2 Safety Audit																													
67	GW3	0 days	Fri 16/02/18	Fri 16/02/18		GW3 16/02																													
68	<b>Procurement</b>	<b>39 days</b>	<b>Mon 29/01/18</b>	<b>Thu 22/03/18</b>		Procurement																													
69	Determine procurement route	0.8 wks	Mon 29/01/18	Thu 01/02/18	67FF-10 days	Determine procurement route																													
70	Start procurement	0 days	Thu 01/02/18	Thu 01/02/18	69	Start procurement 01/02																													
71	Tender Brief	2 wks	Fri 02/02/18	Thu 15/02/18	70	Tender Brief																													
72	Tender Responses	4 wks	Fri 16/02/18	Thu 15/03/18	71	Tender Responses																													
73	Review Responses	5 days	Fri 16/03/18	Thu 22/03/18	72	Review Responses																													
74	Award	0 days	Thu 22/03/18	Thu 22/03/18	73	Award 22/03																													
75	<b>Road Space Restraints</b>	<b>53 days?</b>	<b>Thu 28/06/18</b>	<b>Mon 10/09/18</b>		Road Space Restraints																													
76	Festival of Speed (tbc)	4 days?	Thu 28/06/18	Tue 03/07/18		Festival of Speed (tbc)																													
77	Glorious Goodwood (tbc)	5 days?	Tue 31/07/18	Mon 06/08/18		Glorious Goodwood (tbc)																													
78	Goodwood Revival (tbc)	2 days?	Fri 07/09/18	Mon 10/09/18		Goodwood Revival (tbc)																													
79	<b>Construction</b>	<b>221 days</b>	<b>Fri 30/03/18</b>	<b>Fri 01/02/19</b>	<b>74FS+5 days</b>	Construction																													
80	Book Road Space	3 mons	Fri 30/03/18	Thu 21/06/18		Book Road Space																													
81	GW4	0 days	Thu 21/06/18	Thu 21/06/18	80	GW4 21/06																													
82	Commence Construction	0 days	Mon 17/09/18	Mon 17/09/18		Commence Construction 17/09																													
83	Construct	5 mons	Mon 17/09/18	Fri 01/02/19	82	Construct																													
84	Complete construction	0 days	Fri 01/02/19	Fri 01/02/19	83	Complete construction 01/02																													
85	GW5	0 days	Fri 01/02/19	Fri 01/02/19	84	GW5 01/02																													
86																																			
87	<b>Post Construction</b>	<b>50 days</b>	<b>Mon 04/02/19</b>	<b>Fri 12/04/19</b>		Post Construction																													
88	Stage 3 Safety Audit	5 days	Mon 11/02/19	Fri 15/02/19	84FS+5 days,85	Stage 3 Safety Audit																													
89	Post construction Admin	10 wks	Mon 04/02/19	Fri 12/04/19	85	Post construction Admin																													
90	Final Accounts	0 days	Fri 12/04/19	Fri 12/04/19	89	Final Accounts 12/04																													

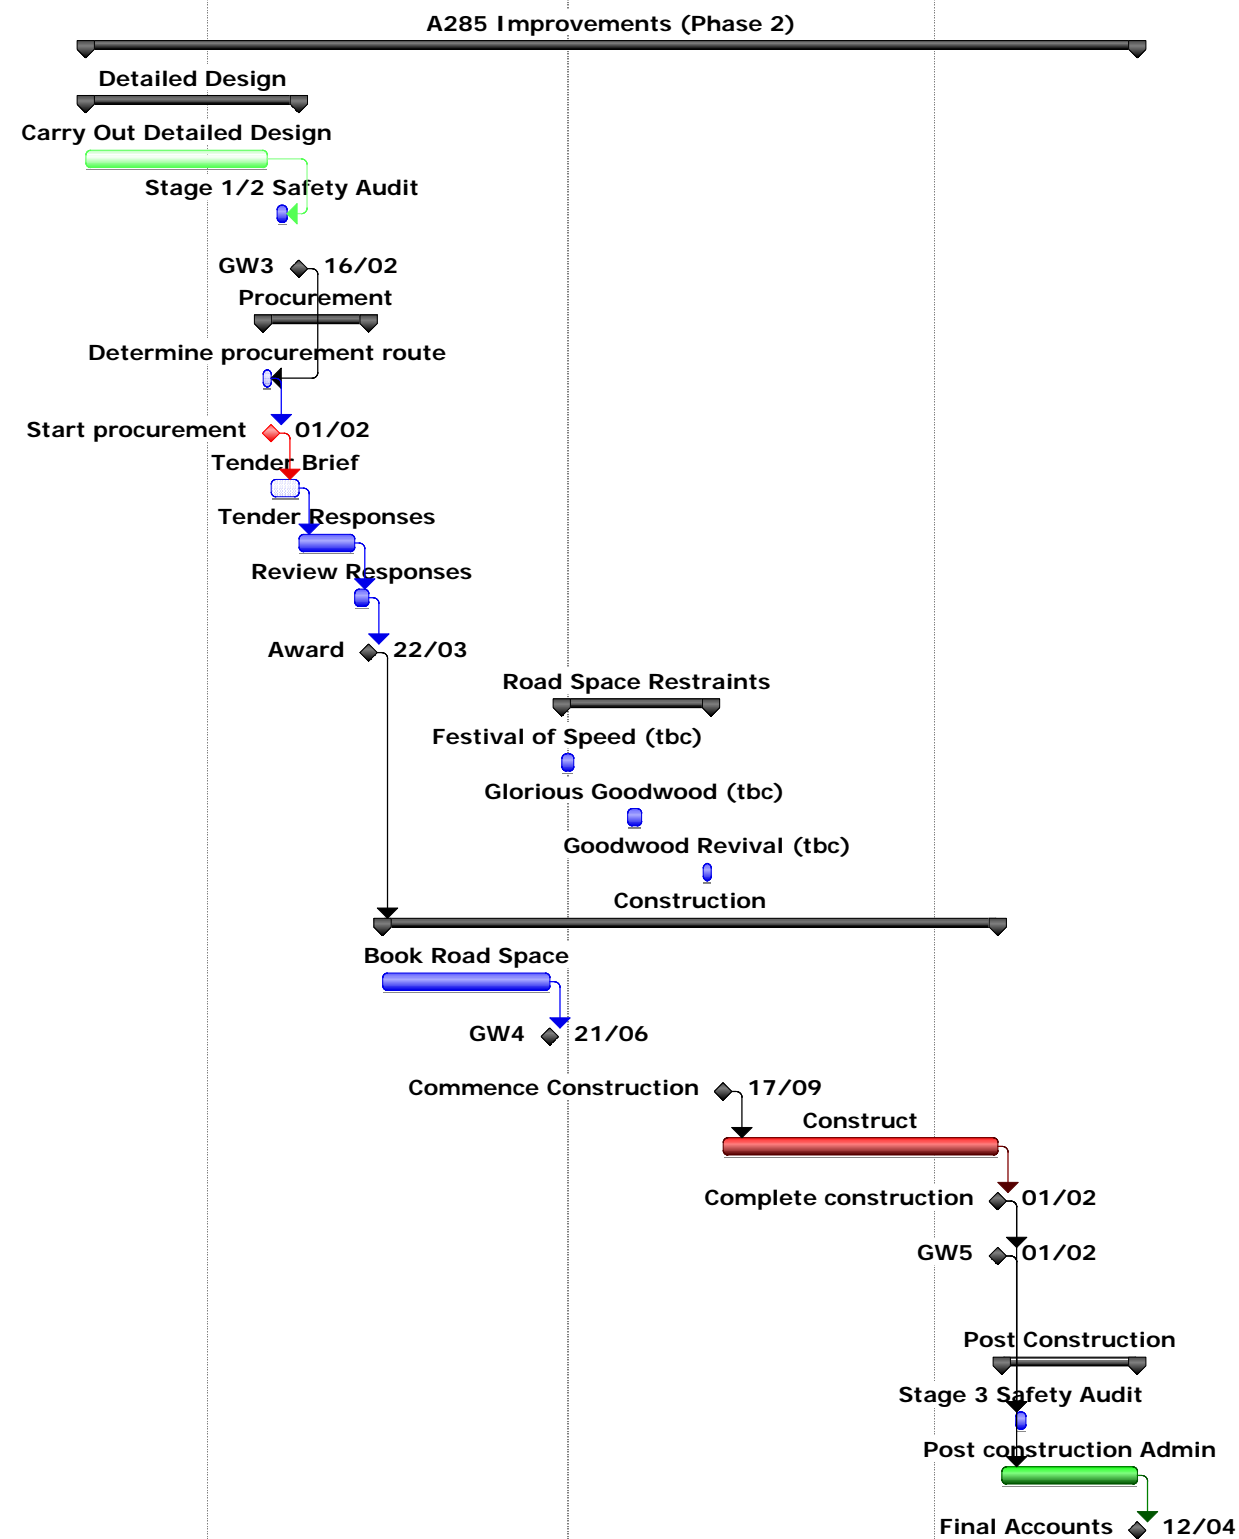

Project: A285 programme v3.pdf  
Date: Fri 28/04/17

Task		Progress		Summary		External Tasks		Deadline	
Split		Milestone		Project Summary		External Milestone			
